

AI Device Inspector Statement of Work.

This Statement of Work sets out the deliverables, acceptance criteria, timeline, responsibilities and commercial terms for the design, build and delivery of the AI Device Inspector platform. It operationalises the accompanying platform proposal and, once signed, governs the engagement.

CLIENT
Hugo Martinez
SUPPLIER
Pixorama Group
DOCUMENT
SOW-2026-011 · v1.0
DATE OF ISSUE
24 July 2026
ENGAGEMENT
Fixed scope · 12 weeks
RELATED DOCUMENT
AI Device Inspector – Platform Proposal
STATUS
For review & signature – supersedes prior scope discussions on execution



Introduction

This document is the definitive statement of what Pixorama will deliver, how each deliverable will be accepted, and the terms under which the work proceeds.

Where this Statement of Work and the platform proposal differ, this document prevails on matters of scope, acceptance, schedule and commercials. Anything not expressly listed as in scope in Section 05 or 06 is out of scope and is handled through the change-control process in Section 14.

01 Scope

Sections 04–06 define exactly what is built; Section 07 states what is not.

02 Delivery

Sections 10–11 set the method, timeline and milestones.

03 Acceptance

Sections 12–13 define how deliverables are tested and signed off.

04 Commercials

Sections 14–16 govern change, payment and warranty.

Definitions

Capitalised terms used throughout this document carry the meanings below.

Platform

The AI Device Inspector software system described in Sections 04–06, in all its surfaces (station kiosk, back-office application, client portal) and services.

Deliverable

A discrete, identified output listed in Section 05 or 06, each with its own acceptance basis.
Edge Node The on-site hardware and software that owns the cameras and runs inference at a facility.
Detection A single defect identified by the model on a captured image, with class, confidence, severity and region.
Grade Profile A configurable, versioned rule set that converts a confirmed defect set into a commercial grade for a given buyer.
Holdout Set A frozen, labelled sample of images used once to measure model accuracy and never used for training.
UAT User Acceptance Testing – structured testing performed by the Client’s own operators and supervisors against agreed scripts.
Go-Live The point at which the Platform is used to process live production stock on at least one line.
Business Day Monday to Friday excluding public holidays in the Client’s jurisdiction.

03

W H Y

Project objectives

The Platform is accepted as meeting its purpose when it delivers against these objectives, evidenced by the acceptance criteria in Sections 12–13.

- ☒ **Consistent grading**
One model and one rule set applied to every device, independent of operator or shift.



Speed

Capture-to-grade in under 60 seconds per device on the target hardware.



Defensibility

Every grade backed by photographs, a defect map and a complete audit trail.



Measurable accuracy

Detection performance proven against a frozen holdout set to an agreed threshold.



Operational visibility

Throughput, yield and defect trends visible to supervisors and administrators.



Integration

Records flow to the Client's existing systems without manual re-keying.

04

WHAT IS BEING BUILT

Scope overview

The engagement delivers a production-ready, multi-tenant platform of **12 functional modules** comprising **60 features**, organised for delivery into six

workstreams, plus the AI model, infrastructure and documentation. The detailed deliverables follow in Section 05; the technical deliverables in Section 06.		
WS 1 Foundations Access, roles, tenancy, environments, design system, app shell.	WS 2 Capture Inspection station and the six-angle capture workflow.	WS 3 AI engine Detection model, inference service and the training loop.
WS 4 Review & grading Annotation, correction, grading engine and disposition.	WS 5 Records & data History, reporting, imports, exports and integrations.	WS 6 Insight & admin Dashboard, analytics, administration and audit.

Detailed deliverables

Every deliverable below is committed to the build and is individually acceptance-tested. Deliverable IDs (D-xx) are referenced by the acceptance and milestone schedules.

WS1 Platform foundations			MODULES 01
ID	DELIVERABLE	INCLUDES	ACCEPTANCE BASIS
D-01	Access & authentication	Email/password with optional 2FA; enterprise SSO (SAML 2.0 / OIDC); rotating session tokens.	A user signs in by each method and receives correct role and tenant context.
D-02	Roles & permissions	Operator, Supervisor, Admin and Client roles with a published permission matrix enforced server-side.	Automated per-role permission tests pass; forbidden actions are refused by the API.

ID	DELIVERABLE	INCLUDES	ACCEPTANCE BASIS
D-03	Multi-tenant isolation	Row-level security so one client's data is never returned to another.	Cross-tenant access tests return no data; verified in security testing (Section 13).
D-04	Station kiosk sessions	Device-bound tokens, idle lock, fast operator switching.	A station authenticates as a device; operators switch without full re-login; idle lock engages.
D-05	Design system & app shell	Token set (colour, type, spacing, motion), component library, navigation and layouts for all three surfaces.	Component library published; all subsequent screens assembled from it.

WS2 Inspection station & capture

MODULE 03

ID	DELIVERABLE	INCLUDES	ACCEPTANCE BASIS
D-06	Guided capture workflow	Six-state flow: scan → verify → position → capture → analyse → review.	An operator completes the full flow for a device end to end on station hardware.
D-07	Device identification	Barcode/QR scan and OCR service-tag reading, with manual entry fallback and device lookup (model, spec, prior inspections, warranty).	A scanned device resolves to its record; manual entry works where scan fails.
D-08	Six-angle capture	Single-trigger capture of six angles with per-angle retake and focus/exposure validation.	All six angles captured; blurred/over-exposed frames are rejected and re-shot.
D-09	Offline tolerance	Local capture queue with automatic sync on reconnect.	Captures taken with the network disabled complete and sync when it returns.

ID	DELIVERABLE	INCLUDES	ACCEPTANCE BASIS
D-10	Defect taxonomy	20+ classes across cosmetic, display and hardware, signed off with the Client.	Taxonomy document approved by the Client in writing.
D-11	Detection model	Segmentation + classification, fine-tuned on Client intake photography; per-detection confidence, four-level severity, bounding region and heat map.	Model returns detections on live captures; accuracy gate in Section 13 met.
D-12	Inference service	Model served on the Edge Node GPU, with confidence thresholds and auto-escalation to review.	Inference completes within the per-image time budget on target hardware.
D-13	Model versioning & retrain loop	Every result stamped with its model version; operator corrections queued into the training set; candidate-vs-incumbent evaluation.	Results carry a version; a retrain run is demonstrated against the holdout set.

WS4 Review, grading & disposition

ID	DELIVERABLE	INCLUDES	ACCEPTANCE BASIS
D-14	Annotated review viewer	Bounding boxes, heat-map toggle, zoom-to-defect; cursor tool to resize an AI region or draw a missed one on the photo.	An operator resizes and draws regions; changes persist and are audited.
D-15	Detection management	Accept, reject, reclassify, change severity, merge duplicates; low-confidence queue with supervisor routing.	Each action updates the record and writes an audit entry.
D-16	Grading engine	Cosmetic and functional grades (A-F) and a 0-100 health score from configurable rules; per-client grade profiles.	A confirmed defect set produces the expected grade for a given profile.

ID	DELIVERABLE	INCLUDES	ACCEPTANCE BASIS
D-17	Disposition & override	Recommended disposition (resell / repair / parts / recycle); supervisor override with mandatory reason code.	Overrides require a reason and are captured in the record.

WS5 Records, reporting & data

MODULES 07-09

ID	DELIVERABLE	INCLUDES	ACCEPTANCE BASIS
D-18	Inspection history	Virtualised 16-column grid for 100k+ records; global search, advanced filters, saved presets, bulk actions, role-gated inline editing, saved views.	Grid performs at target with a representative dataset; filters and bulk actions behave.
D-19	Inspection record & report	Tabbed record (overview, images, AI results, audit, edit); full-res viewer; branded PDF certificate with tamper-evident hash; expiring read-only share link.	A certificate generates with correct data and hash; a share link expires as configured.
D-20	Import & export	Five-step CSV import wizard; export to CSV, XLSX, PDF and JSON, filtered or bulk.	A sample file imports with validation; exports produce correct content in each format.
D-21	Integrations	REST API with OpenAPI spec and signed webhooks; one ERP/WMS connector; ZPL label printing; scheduled buyer feeds (SFTP/S3).	A record change fires a signed webhook; the connector posts to the agreed endpoint.

WS6 Insight & administration

MODULES 02, 10-12

ID	DELIVERABLE	INCLUDES	ACCEPTANCE BASIS
D-22	Dashboard & live floor	Live station tiles, shift KPIs, throughput and defect-mix charts, alert feed, operator activity summary.	Dashboard reflects live station state and correct KPIs for a shift.

ID	DELIVERABLE	INCLUDES	ACCEPTANCE BASIS
D-23	Analytics	Throughput, cycle time, yield and rework by station/shift; grade distribution; defect Pareto by supplier; AI-vs-human agreement; date ranges, CSV export, scheduled digest.	Reports compute correctly against known data; digest is delivered on schedule.
D-24	Administration	Client, user, role and station management with camera calibration; taxonomy and severity-rule editor; grade-profile builder with historic preview; notification rules; per-client branding; feature flags.	An administrator configures each area; changes take effect without a release.
D-25	Audit & compliance	Immutable audit log (actor, action, before, after, timestamp), exportable; retention/purge and right-to-erasure; encryption in transit and at rest; field-level redaction for Client-role users.	Every material change is logged; retention and erasure workflows execute; redaction applies.

06

BUILD & HAND-OVER

Technical deliverables

Beyond the functional modules, the engagement delivers the following engineering and documentation assets.

FRONT END

- Next.js 16 / React 19 / TypeScript application serving station, back-office and client-portal surfaces
- Tokenised design system on Tailwind v4; dark-first station UI
- Virtualised data grids (100k+ rows), real-time station status (WebSocket + SSE fallback)
- Offline-tolerant capture (service worker + IndexedDB)
- WCAG 2.2 AA on operator and supervisor journeys; LCP < 2.0s, INP < 200ms budgets

BACK END

- NestJS / TypeScript API with OpenAPI specification
- PostgreSQL 16 with row-level security; Redis + BullMQ job queue
- S3-compatible object storage with presigned uploads
- Python FastAPI inference service; TensorRT model serving on the Edge Node
- Transactional-outbox webhooks; headless-Chromium PDF reporting

INFRASTRUCTURE & OPERATIONS

- Dockerised services; Terraform-defined environments (staging + production)
- GitHub Actions CI/CD with SCA, SAST and secret scanning
- OpenTelemetry tracing to Grafana; Sentry error tracking
- Cloud control plane plus one on-site Edge Node configuration
- Nightly point-in-time backups with a 30-day recovery window

DOCUMENTATION & ENABLEMENT

- Architecture overview and data-model reference
- API reference (OpenAPI) and integration/webhook guide
- Administrator, supervisor and operator user guides
- Model retraining and evaluation guide
- Operational runbooks and recorded training walkthroughs

07

EXCLUSIONS

Out of scope

The following are explicitly excluded from this Statement of Work. Any of them may be added later under change control (Section 14).

NOT INCLUDED

- Native mobile applications – the web app is responsive and installable
- Automated repair-cost estimation and parts pricing
- Marketplace listing sync (eBay, Back Market and similar)

- Interface languages other than English

NOT INCLUDED

- Robotic device handling and conveyor control
- Functional/electrical testing of the device itself (battery cycles, port continuity, screen response)
- Integrations beyond the one ERP/WMS endpoint in D-21
- Procurement of camera, lighting or GPU hardware
- Ongoing managed hosting or a support retainer beyond warranty (Section 16)

08

BASIS OF ESTIMATE

Assumptions & dependencies

The scope, timeline and price in this document rely on the following. A material change to any of them is handled under change control.

ASSUMPTIONS

- The Client provides sample devices covering its real intake mix, plus 1,500–3,000 photographs for training
- Camera rig, lighting and GPU hardware are procured by the Client and on site by Week 3
- One ERP/WMS integration endpoint is in scope
- Interface and documentation are English-only
- Cloud hosting and third-party licences are billed to the Client at cost

CLIENT DEPENDENCIES

- Defect taxonomy and grading rules signed off in Week 1
- Two operators and one supervisor available for one day per sprint (labelling, review, UAT)
- Timely access to environments, the SSO tenant and the integration endpoint
- Decisions and approvals returned within two Business Days of request
- A nominated Client project owner empowered to accept deliverables

EFFECT OF DELAY

Where a Client dependency is not met by the date required, Pixorama will notify the Client; affected milestone dates move by the period of the delay, and any resulting standing time is handled under change control.

09

WHO DOES WHAT

Responsibilities

Obligations are stated at the level of each party. Pixorama resources the engagement at its own discretion to meet the deliverables and dates in this document.

PIXORAMA WILL


- Design, build, test and deliver all deliverables in Sections 05–06
- Train and evaluate the detection model to the accuracy gate in Section 13
- Run system and integration testing, and support Client UAT
- Provide the documentation and training in Section 06
- Report progress on an agreed cadence and maintain the change log and risk register
- Nominate a single point of contact for the Client

THE CLIENT WILL

- Provide sample devices, training photography and the signed-off taxonomy and grading rules
- Procure and install the camera, lighting and GPU hardware by Week 3
- Make operators and a supervisor available for labelling, review and UAT
- Provide access to environments, the SSO tenant and the integration endpoint
- Review deliverables and return acceptance decisions within the windows in Section 12
- Nominate an empowered project owner to accept deliverables and resolve escalations

Delivery approach & timeline

Twelve weeks: four two-week sprints to feature-complete, then a four-week test and acceptance phase. Each sprint ends in a working demo on staging and a stated exit criterion. Code freezes at the end of Week 8.

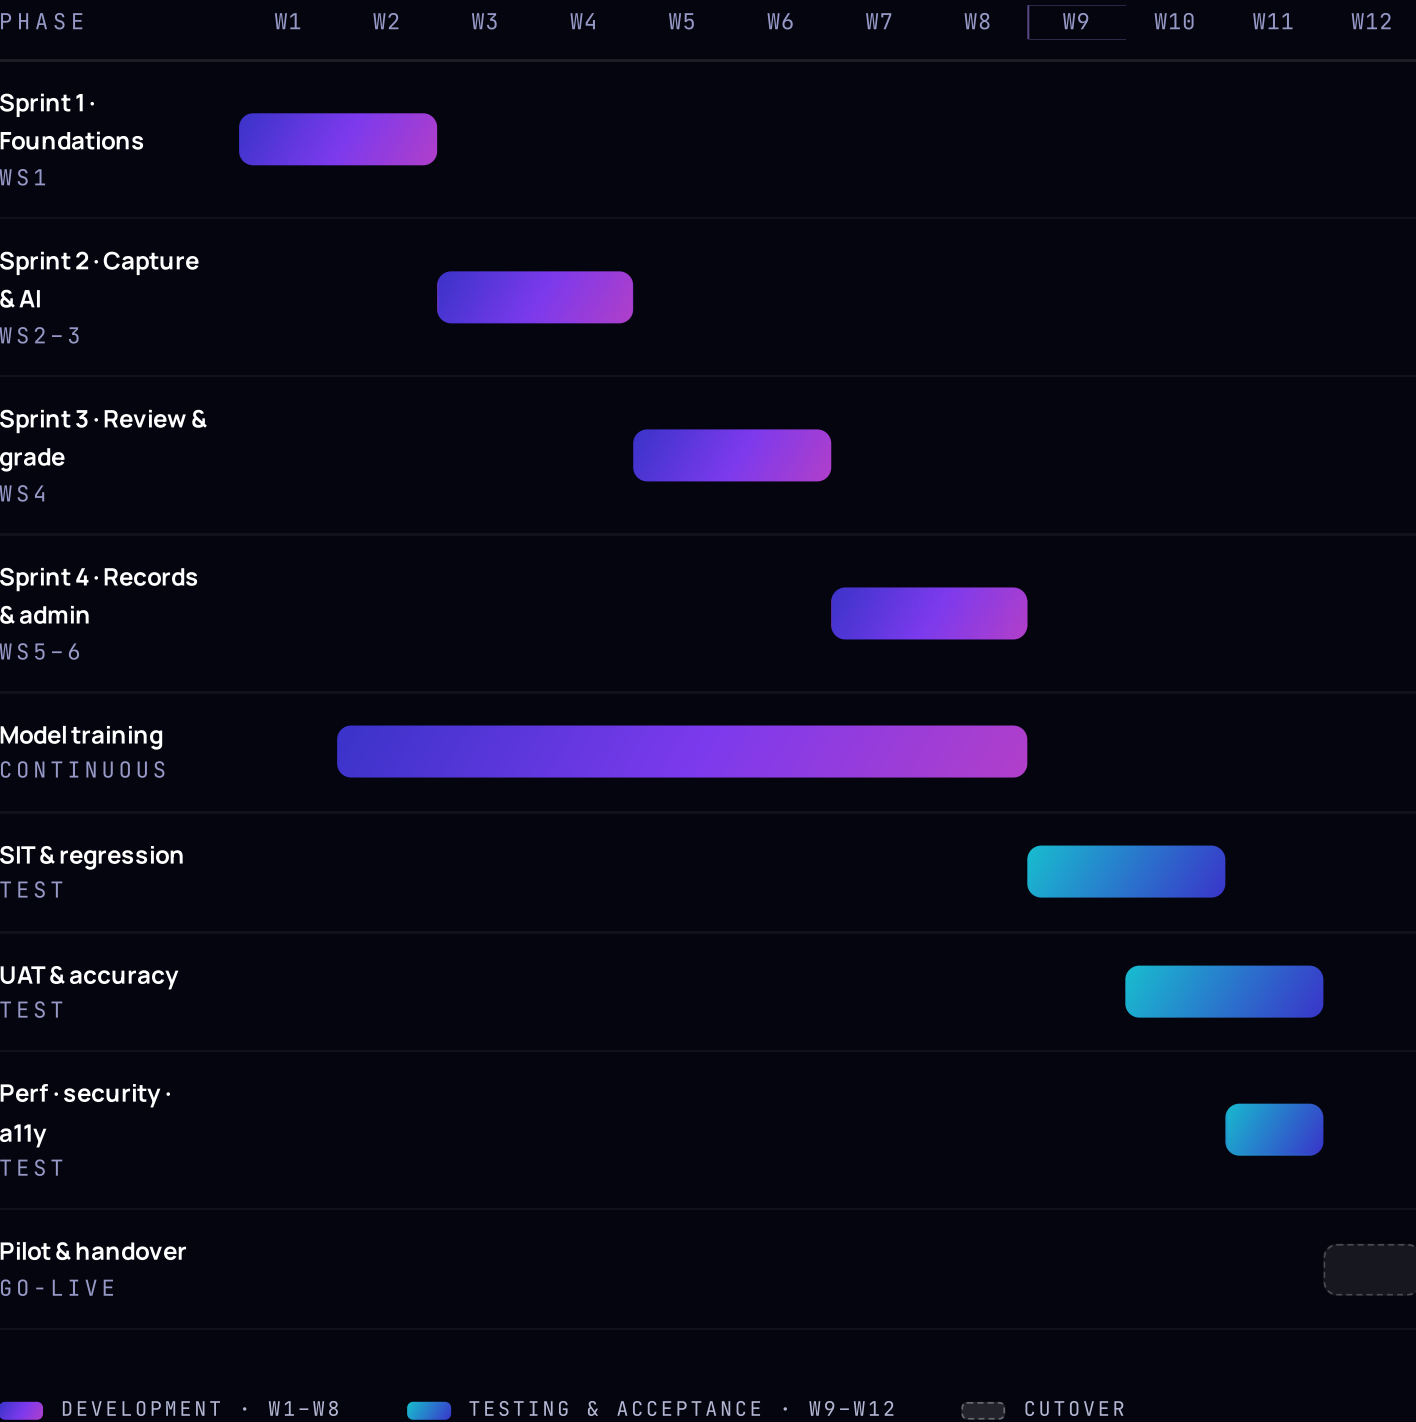

Milestones & deliverable schedule

Each milestone is either a demonstration (Demo) or a formal gate (Gate). Payment is linked to the milestones marked in Section 15.

ID	MILESTONE	DELIVERABLES	TIMING · TYPE
M1	Foundations live	D-01...D-05 – environments, auth, RBAC, app shell; taxonomy sign-off underway.	End W2 · Demo
M2	First device graded	D-06...D-13 – capture and the AI pipeline; a real device returned with detections.	End W4 · Demo
M3	Review & grading	D-14...D-17 – annotation, correction, grading engine and disposition.	End W6 · Demo
M4	Feature complete	D-18...D-25 – records, data, dashboard, analytics, admin, audit. Code freeze.	End W8 · Gate
M5	UAT & accuracy signed off	UAT passed; model meets the accuracy gate in Section 13.	End W10 · Gate
M6	Production go-live & handover	Pilot line stable; documentation and training delivered; handover accepted.	End W12 · Gate

Acceptance process & criteria

How each deliverable and milestone is reviewed, corrected and accepted.

- 01

Review window

On submission of a deliverable, the Client has **five Business Days** to review it against its acceptance basis (Section 05) and either accept it or issue a written list of defects referencing specific criteria.
- 02

Correction

Pixorama corrects valid defects and re-submits. The review window restarts for the re-submitted deliverable, limited to the previously raised items.
- 03

Deemed acceptance

A deliverable is deemed accepted if the Client raises no written defects within the review window, or if it is used in production.
- 04

Partial acceptance

A deliverable is not rejected as a whole for minor (S3/S4) defects; it is accepted with those items logged for correction inside the warranty period.
- 05

Milestone gates

Gate milestones (M4–M6) require the associated deliverables to be accepted and the relevant tests in Section 13 to have passed.

Defect severity & correction targets

S1 · CRITICAL

Blocks core use

Capture, grading or data integrity is unusable, with no workaround.

Fix: same Business Day

S2 • MAJOR

Serious impairment

A key function fails or a workaround is costly.

Fix: 2 Business Days

S3 • MINOR

Limited impact

A non-critical issue with an easy workaround.

Fix: next release

S4 • COSMETIC

Trivial

Visual or textual polish; no functional impact.

Fix: as scheduled

13

FOUR-WEEK TEST PHASE

Testing & quality assurance

Testing is a resourced, gated phase – not a hope. Each gate below must pass before the associated milestone is accepted.

W9

System & regression

Full SIT across station, API, inference and integrations; automated regression on a frozen build.

W10

UAT & accuracy

Client-run UAT scripts on real stock; model scored on the frozen holdout set.

W11

Perf · security · a11y

Load and soak tests; third-party penetration test; WCAG 2.2 AA audit; failure drills.

W12

Pilot

One live line, monitored, with the prior process running alongside.

Acceptance gates

QUANTIFIED THRESHOLDS

- Detection **recall** ≥ 0.90 and **precision** ≥ 0.85 on the top ten defect classes, measured on the holdout set
- API **p95** < 300 ms at 3× expected peak throughput
- Zero open **S1/S2** defects; regression suite green on three consecutive runs
- No **critical or high** security findings open
- WCAG 2.2 AA audit passed on operator and supervisor journeys

EVIDENCE PROVIDED

- Per-class model scorecard against the holdout set
- Grade-agreement study – platform grade vs expert human grade
- Load and soak test reports
- Penetration test report and remediation log
- UAT results with a fix-or-defer decision on every item

14

MANAGING SCOPE

Change control

The deliverables in Sections 05–06 are the agreed scope. Any change to them follows this process; nothing outside it alters price or timeline.

01 Raising a change

Either party may raise a change request in writing, describing the change and its reason.

02 Impact assessment

Pixorama assesses the impact on scope, timeline and price and issues a change note, normally within three Business Days.

03 Approval

Work on a change begins only once the Client approves the change note in writing. Approved changes are appended to this Statement of Work.

04 Swaps

By agreement, a new item of equivalent size may be exchanged for an unstarted deliverable at no change to price or timeline.

05 Standing changes

Rules, taxonomy, grade profiles and branding are configurable and are changed by the Client without a release – these are not change requests.

15

FEES & PAYMENT

Commercials & payment schedule

The engagement is delivered for a fixed fee against the fixed scope in this document. Payment is linked to milestone acceptance. Figures are completed on execution.

TRIGGER	MILESTONE	SHARE	AMOUNT
Mobilisation	On signature of this SOW	15%	[]
M2 · End W4	First device graded end to end	15%	[]
M3 · End W6	Review & grading accepted	15%	[]
M4 · End W8	Feature complete · code freeze	20%	[]
M5 · End W10	UAT & accuracy signed off	15%	[]
M6 · End W12	Go-live & handover accepted	15%	[]
Warranty end	End of the warranty period (Section 16)	5%	[]
Total	Fixed engagement fee	100%	[total]

Amounts, currency, tax treatment and invoice terms are inserted on execution and are governed by the parties' master agreement. Cloud hosting and third-party licences are billed to the Client at cost and are additional to the fixed fee. Invoices are payable within the agreed terms of each accepted milestone.

16

AFTER GO-LIVE

Warranty, support & IP

01 Hypercare

Thirty days of close monitoring and priority defect response from Go-Live, at no additional cost.

02 Warranty period

Ninety days from Go-Live during which S1 and S2 defects in delivered scope are corrected at no cost.

03 Exclusions

Warranty excludes issues caused by Client changes to configuration, unsupported environments, or third-party systems outside the delivered scope.

04 Ongoing support

Support or a managed-service arrangement beyond warranty is available under a separate agreement.

01 Ownership

On full payment, intellectual property in the bespoke deliverables and the trained model weights transfers to the Client.

02 Pre-existing IP

Pixorama retains its pre-existing tools, libraries and know-how, and grants the Client a licence to use them as embedded in the deliverables.

03 Third-party components

Open-source and third-party components remain under their own licences, disclosed on handover.

04 **Confidentiality & data**

Each party protects the other’s confidential information; personal data is handled per the parties’ data-processing terms.

PRECEDENCE

This Statement of Work governs scope, acceptance, schedule and commercials for this engagement. Legal terms (liability, warranties, IP, data protection, termination) are governed by the parties’ master services agreement; where that agreement is silent, the clauses above apply. Nothing here is legal advice, and the parties should have this document reviewed before signature.

17

RUNNING THE ENGAGEMENT

Governance & reporting

- ☒ **Weekly demo**
A working demonstration on staging at the end of each week.
- ☒ **Written status**
A weekly note covering progress, upcoming work, risks and any blocked dependencies.
- ☒ **Shared board**
A live board the Client can view at any time.
- ☒ **Single points of contact**
Each party nominates one contact for day-to-day decisions.
- ☒ **Change & risk logs**
Maintained throughout and reviewed at the weekly checkpoint.
- ☒ **Escalation**
Unresolved items escalate to each party’s nominated owner within two Business Days.

18

MANAGED OPENLY

Key risks & mitigation

RISK	LEVEL	MITIGATION
Insufficient labelled training data	HIGH	Pretrained backbone; Week-1 labelling sprint; active learning from operator corrections; sub-threshold detections route to human review.
Hardware arrives late	HIGH	Mock camera driver and recorded image set in Sprint 2; hardware spec frozen at Week 3; software never blocked on hardware.
Lighting / positioning variance	MEDIUM	Fixed rig geometry, per-station calibration, automatic exposure/focus validation.
Integration access delayed	MEDIUM	Contract-first connector against an agreed schema with a stub; swapped to live on credentials. Not on the critical path.
Scope growth	MEDIUM	Fixed deliverable list; change control (Section 14); equal-size swaps.
Operator adoption	LOW	Client operators involved from Week 1, in every demo, and run UAT themselves.

19

AUTHORISATION

Acceptance & signature

By signing below, each party agrees to the scope, deliverables, acceptance criteria, timeline and commercial terms set out in this Statement of Work.

ACCEPTED FOR THE CLIENT

Hugo Martinez

Signature · Date

Authorised signatory

Signature · Date

